THIS REPORT IS PROVIDED AS AN EXAMPLE ONLY. ALL PROJECT INFORMATION, NAMES, AND DATES ARE FICTITIOUS. THIS IS NOT INTENDED TO BE A FINAL REPRESENTATION OF THE WORK DONE OR RECOMMENDATIONS MADE BY CALTRANS FOR AN ACTUAL PROJECT.

Short Form - Storm Water Data Report

Dist-County-Route: 11-SD-94
Post Mile Limits: 1.5 / R13.4
Project Type: Freeway Maintenance Access
Project ID (or EA): 11-XXXXXX
Program Identification: 20.10.201.230
Phase: ☐ PID
☒ PA/ED
☐ PS&E

Regional Water Quality Control Board(s): San Diego (Region 9)

1.	Is the project required to consider incorporating Treatment BMPs?	Yes ☐	No ☒
2.	Does the project disturb 5 or more acres of soil?	Yes ☐	No ☒
3.	Does the project disturb more than 1 acre of soil and not qualify for the Rainfall Erosivity Waiver?	Yes ☐	No ☒
4.	Does the project potentially create permanent water quality impacts?	Yes ☐	No ☒
5.	Does the project require a notification of ADL reuse	Yes ☐	No ☒

If the answer to any of the preceding questions is "Yes", prepare a Long Form – Storm Water Data Report.

Estimate Construction Start Date: June 2011 Construction Completion Date: August 2011

Separate Dewatering Permit (if yes, permit number) Yes ☐ Permit #_____ No ☒

Erosivity Waiver Yes ☐ Date: _____ No ☒

This Short Form – Storm Water Data Report has been prepared under the direction of the following Licensed Person. The Licensed Person attests to the technical information contained herein and the data upon which recommendations, conclusions, and decisions are based. Professional Engineer or Landscape Architect stamp required at PS&E.

Betsy Ross 9-23-10

Betsy Ross, Registered Project Engineer/Landscape Architect *Date*

I have reviewed the storm water quality design issues and find this report to be complete, current and accurate:

Friedrich Wilhelm von Steuben 9-23-10

Friedrich Wilhelm von Steuben, District/Regional SW Coordinator or Designee *Date*

[Stamp Required for PS&E only)

EXAMPLE ONLY

1. Project Description

This access project proposes to construct seven maintenance vehicle pullouts and eight temporary chain link walk gates on Route 94 in San Diego County. Project limits are approximately the Interstate 5 interchange (PM 1.5) in San Diego to the Kenwood Drive overpass (PM R13.4) in Spring Valley. The purpose of this project is to improve maintenance safety. The project will maintain original line, grade, and hydraulic capacity.

This project includes 15 sites. 8 of the sites are more than 1/4 mile apart which is defined as non-contiguous per the Environmental Protection Agency (EPA) requirements and definitions for the Construction General Permit (CGP). Non-contiguous sites are treated as separate plans of development in accordance with EPA requirements and therefore, DSA is calculated separately for each site. 7 of the sites are less than 1/4 mile apart which is defined as contiguous per the Environmental Protection Agency (EPA) requirements and definitions for the Construction General Permit (CGP). Contiguous sites are treated as common plans of development in accordance with EPA requirements and therefore, DSA is combined for contiguous sites. (See the EPA CGP website: http://cfpub.epa.gov/npdes/stormwater/cgp.cfm#final2008cgp). The contiguous sites are Sites 1 and 2, Sites 7, 8, and 9, and Sites 14 and 15.

The DSA for each of the contiguous and non-contiguous sites is less than 0.25 acres. See the summary table below. All DSA was calculated using AutoCAD software and aerial photographs. As a result of this project, less than 0.97 acres of impervious area will be added. This increase should have a negligible impact on downstream flow due to the small addition of impervious area compared to the drainage area of the receiving waterbody (<1 acre compared to approximately 2,200 acres for Chollas Creek).

EXAMPLE ONLY

DSA Summary Table						
Site Number	**Activity**	**DSA (ac)**	**PM From**	**PM To**	**Distance Between Activities (mi)**	**Total DSA (ac)**
1	Walk Gate	0.025	1.5	1.8		
					0.2	
2	MVP	0.110	2.0	2.2		0.135
					0.7	
3	Walk Gate	0.025	2.9	3.4		0.025
					0.8	
4	MVP	0.110	4.2	4.5		0.110
					0.4	
5	MVP	0.110	4.9	5.2		0.110
					0.4	
6	MVP	0.110	5.6	5.9		0.110
					1.7	
7	Walk Gate	0.025	7.6	7.9		
					0.2	
8	MVP	0.110	8.1	8.4		
					0.1	
9	Walk Gate	0.025	8.5	9.0		0.160
					0.4	
10	Walk Gate	0.025	9.4	9.7		0.025
					0.5	
11	Walk Gate	0.025	10.2	10.3		0.025
					0.6	
12	Walk Gate	0.025	10.9	11.2		0.025
					0.4	
13	Walk Gate	0.025	11.6	12.0		0.025
					0.5	
14	MVP	0.110	12.5	13.0		
					0.1	
15	MVP	0.110	13.1	13.4		0.220

EXAMPLE ONLY

The project is located in the Chollas hydraulic sub-area (HAS) 908.22 and the La Nacion HSA 909.12. The receiving waterbody for HSA 908.22 is Chollas Creek and for HSA 909.12 is the San Diego Bay Shoreline. Chollas Creek is an urban creek located within the project limits. A portion of the creek flows parallel to the state right-of-way. The creek is concrete-lined in some locations and unlined in others. The creek flows into the eastern shoreline of the San Diego Bay. Both Chollas Creek and the San Diego Bay Shoreline are 303(d) listed waterbodies. Chollas Creek is listed for copper, lead, zinc, indicator bacteria, and diazinon; a TMDL has been developed for diazinon. The San Diego Bay Shoreline is listed for copper.

There are no high risk areas within the vicinity of the project, and there are no existing permanent storm water treatment BMPs near or within the project limits.

2. Construction Site BMPs

This project has a disturbed soil area of less than 0.25 acres and, therefore, requires the preparation of a Water Pollution Control Program (WPCP). Since the DSA is less that 1.0 acre at each site, risk level determination is not required.

Projects with similar scope and range of construction activities typically require the Construction Site BMPs identified in this section. Soil stabilization and sediment control typically consists of placing linear sediment barriers, such as fiber rolls, around the excavation to provide run-on and run-off control and to prevent concentrated flow from eroding areas of soil disturbance. Storm drain inlet protection will be deployed throughout the project.

Various non-storm water management, waste management, and housekeeping BMPs shall be used throughout the duration of the project and will be included in the Construction Site Management cost item.

The following BMPs will be included as separate bid line items: temporary fiber rolls, temporary drainage inlet protection, stabilized construction entrance/exit, and preparation of a Water Pollution Control Program. The following BMPs will be included as a lump sum under the Construction Site Management item: material delivery and storage, material use, spill prevention and control, and paving and grinding operations. Compliance of the CGP can be met through the use of traditional BMPs, therefore an active treatment system is not required.

A combination of the Historical Project Method (Option 2) and Unit Cost Method (Option 3) were used to estimate costs for Construction Site BMPs. The following quantities for the selected Construction Site BMPs were estimated from take-off measurements using the layout sheets.

BEES	Temporary BMPs - PPDG Appendix C	Quantity	Unit
074028	Temp. Fiber Roll	1,500	ft^2
074038	Temp. Drainage Inlet Protection	20	EA
074033	Stabilized Constr. Entrance/Exit	4	EA
074017	Water Pollution Control Program (WPCP)	1	LS
074016	***Construction Site Management**	1	LS
*CSM**	*Material Delivery and Storage*	*1*	*LS*
*CSM**	*Material Use*	*1*	*LS*
*CSM**	*Spill Prevention and Control*	*1*	*LS*
*CSM**	*Paving & Grinding Operations*	*1*	*LS*

A meeting was held with the District Construction Stormwater Coordinator (CSWC), William Alexander, on September 10, 2010. The meeting was held on site to discuss the temporary construction site BMP implementation strategy and was attended by Betsy Ross (Project Engineer), William Alexander (CSWC), and Paul Revere (District Maintenance Stormwater Coordinator). Topics discussed at the coordination meeting include: construction site BMP selection (including inlet protection) and construction site BMP quantity estimating strategy. Since there are no new inlets, drain inlet stenciling is not required.

Concurrence on the implementation strategy will be obtained during PS&E.

EXAMPLE ONLY

3. Required Attachments

- Vicinity Map
- Evaluation Documentation Form

4. Supplemental Attachments

- Construction Site BMP Consideration Form
- SWDR Tracking Form
- Storm Water BMP Cost Summary
- Checklist CS-1, Parts 1-6 [only those parts that are applicable]

EXAMPLE ONLY

EXAMPLE ONLY

Dist	COUNTY	ROUTE	POST MILES TOTAL PROJECT	SHEET No.	TOTAL SHEETS
11	SD	94	1.5/R13.4	1	1

STATE OF CALIFORNIA

DEPARTMENT OF TRANSPORTATION

PROJECT PLANS FOR CONSTRUCTION ON

STATE HIGHWAY

IN SAN DIEGO COUNTY IN AND NEAR SAN DIEGO, LEMON GROVE, AND LA MESA AT VARIOUS LOCATIONS FROM 0.1 MILE WEST OF 22ND STREET OVERCROSSING TO 0.1 MILE EAST OF AVOCADO BOULEVARD OVERCROSSING

LOCATION MAP

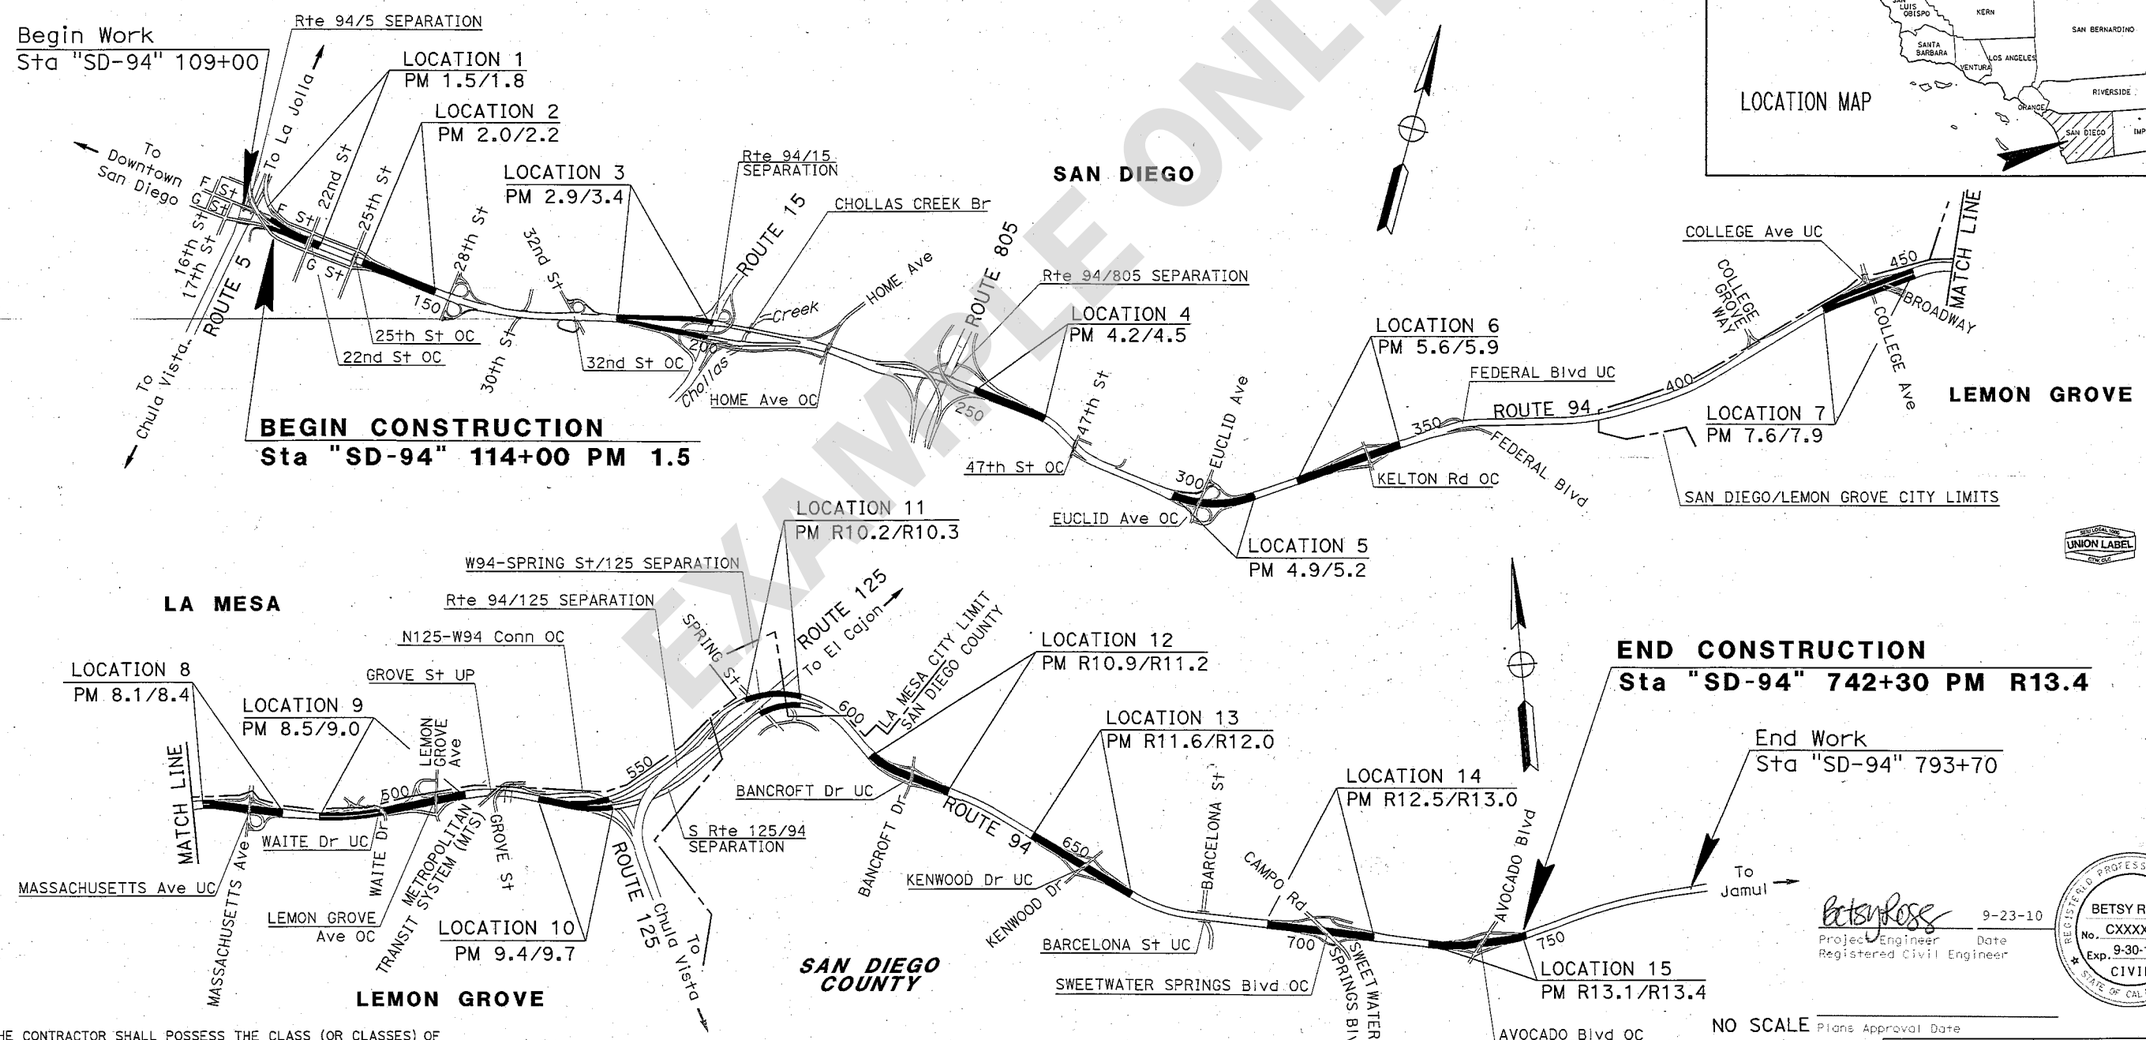

THE CONTRACTOR SHALL POSSESS THE CLASS (OR CLASSES) OF LICENSE AS SPECIFIED IN THE "NOTICE TO BIDDERS."

EXAMPLE ONLY

PROJECT MANAGER: GEORGE WASHINGTON

PROJECT ENGINEER: BETSY ROSS

Betsy Ross 9-23-10
Project Engineer Date
Registered Civil Engineer

REGISTERED PROFESSIONAL ENGINEER — BETSY ROSS — No. CXXXXX — Exp. 9-30-11 — CIVIL — STATE OF CALIFORNIA

NO SCALE Plans Approval Date

CONTRACT No. 11-XXXXXX

LAST REVISION 9-15-10

BORDER LAST REVISED 9-15-10 | CALTRANS WEB SITE IS: HTTP//WWW.DOT.CA.GOV/ | RELATIVE BORDER SCALE IS IN INCHES 0 1 2 3 | USERNAME => s127400 DGN FILE => b26171ta001.dgn | CU XXXXX | EA XXXXXX

EXAMPLE ONLY

DATE: 9-23-10

Project ID (or EA): 11-XXXXXX

NO.	CRITERIA	YES ✓	NO ✓	SUPPLEMENTAL INFORMATION FOR EVALUATION
1.	Begin Project Evaluation regarding requirement for consideration of Treatment BMPs	✓		See Figure 4-1, Project Evaluation Process for Consideration of Permanent Treatment BMPs. Go to 2
2.	Is this an emergency project?		✓	If **Yes**, go to 10. If **No**, continue to 3.
3.	Have TMDLs or other Pollution Control Requirements been established for surface waters within the project limits? Information provided in the water quality assessment or equivalent document.	✓		If **Yes**, contact the District/Regional NPDES Coordinator to discuss the Department's obligations under the TMDL (if Applicable) or Pollution Control Requirements, go to 9 or 4. FWS *(Dist./Reg. SW Coordinator initials)* If **No**, continue to 4.
4.	Is the project located within an area of a local MS4 Permittee?	✓		If **Yes**. *(Cities of San Diego, Lemon Grove, and La Mesa)*, go to 5. If **No**, document in SWDR go to 5.
5.	Is the project directly or indirectly discharging to surface waters?	✓		If **Yes**, continue to 6. If **No**, go to 10.
6.	Is it a new facility or major reconstruction?		✓	If **Yes**, continue to 8. If **No**, go to 7.
7.	Will there be a change in line/grade or hydraulic capacity?		✓	If **Yes**, continue to 8. If **No**, go to 10.
8.	Does the project result in a net increase of one acre or more of new impervious surface?			If **Yes**, continue to 9. If **No**, go to 10. *0.97 (Net Increase New Impervious Surface)*
9.	Project is required to consider approved Treatment BMPs.		See Sections 2.4 and either Section 5.5or 6.5 for BMP Evaluation and Selection Process. Complete Checklist T-1 in this Appendix E.	
10.	Project is not required to consider Treatment BMPs. FWS *(Dist./Reg. Design SW Coord. Initials)* BR *(Project Engineer Initials)* 9-23-10 *(Date)*	✓	Document for Project Files by completing this form, and attaching it to the SWDR.	

See Figure 4-1, Project Evaluation Process for Consideration of Permanent Treatment BMPs

EXAMPLE ONLY

DATE: _____9-23-10_____

Project ID (or EA): _____11-XXXXXX_____

Project Evaluation Process for the Consideration of Construction Site BMPs

NO.	CRITERIA	YES ✓	NO ✓	SUPPLEMENTAL INFORMATION
1.	Will construction of the project result in areas of disturbed soil as defined by the Project Planning and Design Guide (PPDG)?	✓		If Yes, Construction Site BMPs for Soil Stabilization (SS) will be required. Complete CS-1, Part 1. Continue to 2. If No, Continue to 3.
2.	Is there a potential for disturbed soil areas within the project to discharge to storm drain inlets, drainage ditches, areas outside the right-of-way, etc?	✓		If Yes, Construction Site BMPs for Sediment Control (SC) will be required. Complete CS-1, Part 2. Continue to 3.
3.	Is there a potential for sediment or construction related materials and wastes to be tracked offsite and deposited on private or public paved roads by construction vehicles and equipment?	✓		If Yes, Construction Site BMPs for Tracking Control (TC) will be required. Complete CS-1, Part 3. Continue to 4.
4.	Is there a potential for wind to transport soil and dust offsite during the period of construction?	✓		If Yes, Construction Site BMPs for Wind Erosion Control (WE) will be required. Complete CS-1, Part 4. Continue to 5.
5.	Is dewatering anticipated or will construction activities occur within or adjacent to a live channel or stream?		✓	If Yes, Construction Site BMPs for Non-Storm Water Management (NS) will be required. Complete CS-1, Part 5. Continue to 6.
6.	Will construction include saw-cutting, grinding, drilling, concrete or mortar mixing, hydro-demolition, blasting, sandblasting, painting, paving, or other activities that produce residues?	✓		If Yes, Construction Site BMPs for Non-Storm Water Management (NS) will be required. Complete CS-1, Parts 5 & 6. Continue to 7.
7.	Are stockpiles of soil, construction related materials, and/or wastes anticipated?		✓	If Yes, Construction Site BMPs for Waste Management and Materials Pollution Control (WM) will be required. Complete CS-1, Part 6. Continue to 8.
8.	Is there a potential for construction related materials and wastes to have direct contact with precipitation; stormwater run-on, or stormwater runoff; be dispersed by wind; be dumped and/or spilled into storm drain systems?	✓		If Yes, Construction Site BMPs for Waste Management and Materials Pollution Control (WM) will be required. Complete CS-1, Part 6. Continue to 9.
9.	End of checklist.	✓	Document for Project Files by completing this form, and attaching it to the SWDR.	

PE to initialize after concurrence with Construction (PS&E only) *Date*

EXAMPLE ONLY

SWDR Tracking Form

Rpt_to_hq	Dist_EA	District	EA	County	Route	Beg_PM	End_PM	Descrip	Phase	LongSWDR	PhaseRptDate	Exempt	TBMP	Pollution_Program	Disturbance Acr	AddImpArea	PercentTreated	MS4Area	MS4CiCo	ater Bodies Affec	Criteria	BioStrip	BioSwale	Detention	Infiltration	InfilTrench	GSRD	TST	DryWeath	MedFilter	MCTT	WetBasin	Const_Start	Const_Comp	SWComment
23-Sep-10	11-XXXXXX	11	XXXXXX	SD	94	1.5	R13.4	Freeway Maintenance Access	PID	FALSE	23-Sep-10	TRUE	FALSE	SWPPP	1	1	TRUE	Cities of San		Cholla Creek,	303	0	0	0	0	0	0	0	0	0	0	0	01-Jun-11	01-Aug-11	

EXAMPLE ONLY

EXAMPLE ONLY

Storm Water BMP Cost Summary - PA/ED

THIS INFORMATION IS FOR **CALTRANS INTERNAL USE ONLY**

Temporary Construction Site BMPs

BEES	Temporary BMPs - PPDG Appendix C	SSP/nSSP (#, Y or N)	STD. Det. (Y or N)	Quantity	Unit	Unit Cost ($/Unit)	Cost ($)
	Temporary Soil Stabilization						
074028	Temporary Fiber Roll	07-420	Yes	1,500	ft^2	2	$ 2,250
						Subtotal Soil Stabilization BMPs	**$ 2,250**

	Temporary Sediment Control	SSP/nSSP (#, Y or N)	STD. Det. (Y or N)	Quantity	Unit	Unit Cost ($/Unit)	Cost
074038	Temp. Drainage Inlet Protection	07-490	Yes	25	EA	150	$ 3,750
						Subtotal Sediment Control BMPs	**$ 3,750**

BEES	***Temporary Tracking Control***	SSP/nSSP (#, Y or N)	STD. Det. (Y or N)	Quantity	Unit	Unit Cost ($/Unit)	Cost
074033	Stabilized Constr. Entrance/Exit	07-480	Yes	6	EA	5,000	$ 30,000
						Subtotal Tracking Control BMPs	**$ 30,000**

BEES	***Temporary Waste Management Control***	SSP/nSSP (#, Y or N)	STD. Det. (Y or N)	Quantity	Unit	Unit Cost ($/Unit)	Cost
CSM*	Material Delivery and Storage	07-346	No	1	LS		$ -
CSM*	Material Use	07-346	No	1	LS		$ -
CSM*	Spill Prevention and Control	07-346	No	1	LS		$ -
						Subtotal Waste Management & Materials Handling BMPs	**$ -**

BEES	***Temporary Non-Storm Water Management***	SSP/nSSP (#, Y or N)	STD. Det. (Y or N)	Quantity	Unit	Unit Cost ($/Unit)	Cost
CSM*	Paving & Grinding Operations			1	LS		$ -
074016	***Construction Site Management**	07-346	No	1	LS	35,000	$ 35,000
						Subtotal Non-Storm Water Management	**$ 35,000**

BEES	***Miscellaneous Items***	SSP/nSSP (#, Y or N)	STD. Det. (Y or N)	Quantity	Unit	Unit Cost ($/Unit)	Cost
074017	Water Pollution Control Program (WPCP)	07-340	No	1	LS	1,200	$ 1,200
						Subtotal Miscellaneous Items	**$ 1,200**

Total Construction Site BMP Costs	**$ 72,200**

EXAMPLE ONLY

Construction Site BMPs
Checklist CS-1, Part 1

Prepared by: B. Ross Date: 9-23-10 District-Co-Route: 11-SD-94

PM : 1.5 / R13.4 Project ID (or EA): 11-XXXXXX RWQCB: San Diego (9)

Soil Stabilization

General Parameters

1. How many rainy seasons are anticipated between begin and end of construction? 0
2. What is the total disturbed soil area for the project? (ac) <0.25
   (a) How much of the project DSA consists of slopes 4:1 (h:v) or flatter? (ac) <0.25
   (b) How much of the project DSA consists of 4:1 (h:v) < slopes < 2:1 (h:v)? (ac) 0
   (c) How much of the project DSA consists of slopes 2:1 (h:v) and steeper? (ac) 0
   (d) How much of the project DSA consists of slopes with slope lengths longer than 20 ft? (ac) 0
3. What rainfall area does the project lie within? (Refer to Table 2-1 of the Construction Site Best Management Practices Manual) 4
4. Review the required combination of temporary soil stabilization and temporary sediment controls and barriers for area, slope inclinations, rainy and non-rainy season, and active and non-active disturbed soil areas. (Refer to Tables 2-2, and 2-3 of the Construction Site Best Management Practices Manual for Rainfall Area requirements.) ☒ Complete

Scheduling (SS-1)

5. Does the project have a duration of more than one rainy season and have disturbed soil area in excess of 25 acres? ☐ Yes ☒ No
   (a) Include multiple mobilizations (Move-in/Move-out) as a separate contract bid line item to implement permanent erosion control or revegetation work on slopes that are substantially complete. (Estimate at least 6 mobilizations for each additional rainy season. Designated Construction Representative may suggest an alternate number of mobilizations.) ☐ Complete
   (b) Edit Order of Work specifications for permanent erosion control or revegetation work to be implemented on slopes that are substantially complete. ☐ Complete

EXAMPLE ONLY

(c) Edit permanent erosion control or revegetation specifications to require seeding and planting work to be performed when optimal. ☐Complete

Preservation of Existing Vegetation (SS-2)

6. Do Environmentally Sensitive Areas (ESAs) exist within or adjacent to the project limits? (Verify the completion of DPP-1, Part 5) ☐Yes ☒No

   (a) Verify the protection of ESAs through delineation on all project plans. ☐Complete

   (b) Protect from clearing and grubbing and other construction disturbance by enclosing the ESA perimeter with high visibility plastic fence or other BMP. ☐Complete

7. Are there areas of existing vegetation (mature trees, native vegetation, landscape planting, etc.) that need not be disturbed by project construction? Will areas designated for proposed treatment BMPs need protection (infiltration characteristics, vegetative cover, etc.)? (Coordinate with District Environmental and Construction to determine limits of work necessary to preserve existing vegetation to the maximum extent practicable.) ☐Yes ☒No

   (a) Designate as outside of limits of work (or designate as ESAs) and show on all project plans. ☐Complete

   (b) Protect with high visibility plastic fence or other BMP. ☐Complete

8. If yes for 6, 7, or both, then designate ESA fencing as a separate contract bid line item, *if not already incorporated as part of design pollution prevention work (See DPP-1, Part 5).* ☐Complete

Slope Protection

9. Provide a soil stabilization BMP(s) appropriate for the DSA, slope steepness, slope length, and soil erodibility. (Consult with District/Regional Landscape Architect.) **NA**

   (a) Select SS-3 (Hydraulic Mulch), SS-4 (Hydroseeding), SS-5 (Soil Binders), SS-6 (Straw Mulch), SS-7 (Geotextiles, Mats, Plastic Covers, and Erosion Control Blankets), SS-8 (Wood Mulching), other BMPs or a combination to cover the DSA throughout the project's rainy season. ☐Complete

   (b) Increase the quantities by 25% for each additional rainy season. (Designated Construction Representative may suggest an alternate increase.) ☐Complete

   (c) Designate as a separate contract bid line item. ☐Complete

EXAMPLE ONLY

Slope Interrupter Devices

10. Provide slope interrupter devices for all slopes with slope lengths equal to or greater than of 20 ft in length. (Consult with District/Regional Landscape Architect and Designated Construction Representative.) **NA**

    (a) Select SC-5 (Fiber Rolls) or other BMPs to protect slopes throughout the project's rainy season. ☐Complete

    (b) For slope inclination of 4:1 (h:v) and flatter, SC-5 (Fiber Rolls) or other BMPs shall be placed along the contour and spaced 20 ft on center. ☐Complete

    (c) For slope inclination between 4:1 (h:v) and 2:1 (h:v), SC-5 (Fiber Rolls) or other BMPs shall be placed along the contour and spaced 15 ft on center. ☐Complete

    (d) For slope inclination of 2:1 (h:v) and greater, SC-5 (Fiber Rolls) or other BMPs shall be placed along the contour and spaced 10 ft on center. ☐Complete

    (e) Increase the quantities by 25% for each additional rainy season. (Designated Construction Representative may suggest alternate increase.) ☐Complete

    (f) Designate as a separate contract bid line item. ☐Complete

Channelized Flow

11. Identify locations within the project site where concentrated flow from stormwater runoff can erode areas of soil disturbance. Identify locations of concentrated flow that enters the site from outside of the right-of-way (off-site run-on). ☒Complete

    (a) Utilize SS-7 (Geotextiles, Mats, Plastic Covers, and Erosion Control Blankets), SS-9 (Earth Dikes/Swales, Ditches), SS-10 (Outlet Protection/Velocity Dissipation), SS-11 (Slope Drains), SC-4 (Check Dams), or other BMPs to convey concentrated flows in a non-erosive manner. **Fiber rolls** ☒Complete

    (b) Designate as a separate contract bid line item. ☒Complete

EXAMPLE ONLY

Construction Site BMPs
Checklist CS-1, Part 2

Prepared by: B. Ross Date: 9-23-10 District-Co-Route: 11-SD-94

PM : 1.5 / R13.4 Project ID (or EA): 11-XXXXXX RWQCB: San Diego (9)

Sediment Control

Perimeter Controls - Run-off Control

1. Is there a potential for sediment laden sheet and concentrated flows to discharge offsite from runoff cleared and grubbed areas, below cut slopes, embankment slopes, etc.? ☒Yes ☐No

   (a) Select linear sediment barrier such as SC-1 (Silt Fence), SC-5 (Fiber Rolls), SC-6 (Gravel Bag Berm), SC-8 (Sand Bag Barrier), SC-9 (Straw Bale Barrier), or a combination to protect wetlands, water courses, roads (paved and unpaved), construction activities, and adjacent properties. (Coordinate with District Construction for selection and preference of linear sediment barrier BMPs.) **Fiber rolls** ☒Complete

   (b) Increase the quantities by 25% for each additional rainy season. (Designated Construction Representative may suggest an alternate increase.) **NA** ☐Complete

   (c) Designate as a separate contract bid line item. ☒Complete

Perimeter Controls - Run-on Control

2. Do locations exist where sheet flow upslope of the project site and where concentrated flow upstream of the project site may contact DSA and construction activities? ☒Yes ☐No

   (a) Utilize linear sediment barriers such as SS-9 (Earth Dike/Drainage Swales and Lined Ditches), SC-5 (Fiber Rolls), SC-6 (Gravel Bag Berm), SC-8 (Sand Bag Barrier), SC-9 (Straw Bale Barrier), or other BMPs to convey flows through and/or around the project site. (Coordinate with District Construction for selection and preference of perimeter control BMPs.) **Fiber rolls** ☒Complete

   (b) Designate as a separate contract bid line item. ☒Complete

EXAMPLE ONLY

Storm Drain Inlets

3. Do existing or proposed drainage inlets exist within the project limits? ☒Yes ☐No

   (a) Select SC-10 (Storm Drain Inlet Protection) to protect municipal storm drain systems or receiving waters wetlands at each drainage inlet. (Coordinate with District Construction for selection and preference of inlet protection BMPs.) ☒Complete

   (b) Designate as a separate contract bid line item. ☒Complete

4. Can existing or proposed drainage inlets utilize an excavated sediment trap as described in SC-10 (Storm Drain Inlet Protection- Type 2)? ☐Yes ☒No

   (a) Include with other types of SC-10 (Storm Drain Inlet Protection). ☐Complete

Sediment/Desilting Basin (SC-2)

5. Does the project lie within a Rainfall Area where the required combination of temporary soil stabilization and sediment control BMPs includes desilting basins? (Refer to Tables 2-1, 2-2, and 2-3 of the Construction Site Best Management Practices Manual for Rainfall Area requirements.) ☐Yes ☒No

   (a) Consider feasibility for desilting basin allowing for available right-of-way within the project limits, topography, soil type, disturbed soil area within the watershed, and climate conditions. Document if the inclusion of sediment/desilting basins is infeasible. ☐Complete

   (b) If feasible, design desilting basin(s) per the guidance in SC-2 Sediment/ Desilting Basins of the Construction Site BMP Manual to maximize capture of sediment-laden runoff. ☐Complete

   Designate as a separate contract bid item. ☐Complete

6. Is ATS to be used for controlling sediment? ☐Yes ☒No

   (a) If "yes", then will desilting basin or other means of natural storage be used? ☐Yes ☐No

   (b) If "no", then plan for storage tanks sufficient to hold treatment volume. ☐Complet

7. Will the project benefit from the early implementation of proposed permanent Treatment BMPs? (Coordinate with District Construction.) ☐Yes ☒No

   (a) Edit Order of Work specifications for permanent treatment BMP work to be implemented in a manner that will allow its use as a construction site BMP. ☐Complete

Sediment Trap (SC-3)

8. Can sediment traps be located to collect channelized runoff from disturbed soil areas prior to discharge? ☐Yes ☒No

   (a) Design sediment traps in accordance with the Construction Site BMP Manual. ☐Complete

   (b) Designate as a separate contract bid line item. ☐Complete

EXAMPLE ONLY

Construction Site BMPs
Checklist CS-1, Part 3

Prepared by: B. Ross Date: 9-23-10 District-Co-Route: 11-SD-94

PM : 1.5 / R13.4 Project ID (or EA): 11-XXXXXX RWQCB: San Diego (9)

Tracking Controls

Stabilized Construction Entrance/Exit (TC-1)

1. Are there points of entrance and exit from the project site to paved roads where mud and dirt could be transported offsite by construction equipment? (Coordinate with District Construction for selection and preference of tracking control BMPs.) ☒Yes ☐No

   (a) Identify and designate these entrance/exit points as stabilized construction entrances (TC-1). ☒Complete

   (b) Designate as a separate contract bid line item. ☒Complete

Tire/Wheel Wash (TC-3)

1. Are site conditions anticipated that would require additional or modified tracking controls such as entrance/outlet tire wash? (Coordinate with District Construction.) ☐Yes ☒No

   Designate as a separate contract bid line item. ☐Complete

Stabilized Construction Roadway (TC-2)

3. Are temporary access roads necessary to access remote construction activity locations or to transport materials and equipment? (In addition to controlling dust and sediment tracking, access roads limit impact to sensitive areas by limiting ingress, and provide enhanced bearing capacity.) (Coordinate with District Construction.) ☐Yes ☒No

   (a) Designate these temporary access roads as stabilized construction roadways (TC-2). ☐Complete

   (b) Designate as a separate contract bid line item. ☐Complete

Street Sweeping and Vacuuming (SC-7)

1. Is there a potential for tracked sediment or construction related residues to be transported offsite and deposited on public or private roads? (Coordinate with District Construction for preference of including street sweeping and vacuuming with tracking control BMPs.) ☒Yes ☐No

   Designate as a separate contract bid line item. ☒Complete

EXAMPLE ONLY

Construction Site BMPs
Checklist CS-1, Part 4

Prepared by: B. Ross Date: 9-23-10 District-Co-Route: 11-SD-94

PM : 1.5 / R13.4 Project ID (or EA): 11-XXXXXX RWQCB: San Diego (9)

Wind Erosion Controls

Wind Erosion Control (WE-1)

1. Is the project located in an area where standard dust control practices in accordance with Standard Specifications, Section 10: Dust Control, are anticipated to be inadequate during construction to prevent the transport of dust offsite by wind? *(Note: Dust control by water truck application is paid for through the various items of work. Dust palliative, if it is included, is paid for as a separate item.)* ☐ Yes ☒ No

   (a) Select SS-3 (Hydraulic Mulch), SS-4 (Hydroseeding), SS-5 (Soil Binders), SS-7 (Geotextiles, Mats, Plastic Covers, and Erosion Control Blankets), SS-8 (Wood Mulching) or a combination to cover the DSA subject to wind erosion year-round, especially when significant wind and dry conditions are anticipated during project construction. (Coordinate with District Construction for selection and preference of wind erosion control BMPs.) ☐ Complete

   (b) Designate as a separate contract bid line item. ☐ Complete

EXAMPLE ONLY

Construction Site BMPs
Checklist CS-1, Part 5

Prepared by: B. Ross Date: 9-23-10 District-Co-Route: 11-SD-94

PM : 1.5 / R13.4 Project ID (or EA): 11-XXXXXX RWQCB: San Diego (9)

Non-Storm Water Management

Temporary Stream Crossing (NS-4) & *Clear Water Diversion* (NS-5)

1. Will construction activities occur within a waterbody or watercourse such as a lake, wetland, or stream? (Coordinate with District Construction for selection and preference for stream crossing and clear water diversion BMPs.) ☐Yes ☒No

   (a) Select from types offered in NS-4 (Temporary Stream Crossing) to provide access through watercourses consistent with permits and agreements.[1] ☐Complete

   (b) Select from types offered in NS-5 (Clear Water Diversion) to divert watercourse consistent with permits and agreements.[1] ☐Complete

   (c) Designate as a separate contract bid line item(s). ☐Complete

Other Non-Storm Water Management BMPs

2. Are construction activities anticipated that will generate wastes or residues with the potential to discharge pollutants? ☒Yes ☐No

   (a) Identify potential pollutants associated with the anticipated construction activity and select the corresponding BMP such as NS-1 (Water Conservation Practices), NS-2 (Dewatering Operations), NS-3 (Paving and Grinding Operations), NS-7 (Potable Water/Irrigation), NS-8 (Vehicle and Equipment Cleaning), NS-9 (Vehicle and Equipment Fueling), NS-10 (Vehicle and Equipment Maintenance), NS-11 (Pile Driving Operations), NS-12 (Concrete Curing), NS-13 (Material and Equipment Use Over Water), NS-14 (Concrete Finishing), and NS-15 (Structure Demolition/Removal Over or Adjacent to Water).[1] **Paving and grinding operations** ☒Complete

   (b) Verify that costs for non-stormwater management BMPs are identified in the contract documents. Designate BMP as a separate contract bid line item if the requirements in Construction Site Management (SSP 07-346) are anticipated to be inadequate or if requested by Construction. **CSM requirements are adequate** ☒Complete

EXAMPLE ONLY

[1] Coordinate with District Environmental for consistency with US Army Corps of Engineers 404 and 401 permits and Dept. of Fish and Game 1601 Streambed alteration Agreements.

Construction Site BMPs
Checklist CS-1, Part 6

Prepared by: B. Ross Date: 9-23-10 District-Co-Route: 11-SD-94

PM : 1.5 / R13.4 Project ID (or EA): 11-XXXXXX RWQCB: San Diego (9)

Waste Management & Materials Pollution Control

Concrete Waste Management (WM-8)

1. Does the project include concrete placement or mortar mixing? ☐Yes ☒No

   (a) Select from types offered in WM-8 (Concrete Waste Management) to provide concrete washout facilities. In addition, consider portable concrete washouts and vendor supplied concrete waste management services. (Coordinate with District Construction for selection and preference of waste management and materials pollution control BMPs.) ☐Complete

   (b) Designate as a separate contract bid line item if the quantity of concrete waste and washout are anticipated to exceed 5.2 yd^3 or if requested by Construction. ☐Complete

Other Waste Management and Materials Pollution Controls

2. Are construction activities anticipated that will generate wastes or residues with the potential to discharge pollutants? ☒Yes ☐No

   (a) Identify potential pollutants associated with the anticipated construction activity and select the corresponding BMP such as WM-1 (Material Delivery and Storage), WM-2 (Material Use), WM-4 (Spill Prevention and Control), WM-5 (Solid Waste Management), WM-6 (Hazardous Waste Management), WM-7 (Contaminated Soil Management), WM-9 (Sanitary/Septic Waste Management) and WM-10 (Liquid Waste Management) **Material Delivery and Storage, Material Use, Spill Prevention and Control** ☒Complete

   (b) Verify that costs for waste management and materials pollution control BMPs are identified in the contract documents. Designate BMP as a separate contract bid line item if the requirements in Construction Site Management (SSP 07-346) are anticipated to be inadequate or if requested by Construction. **CSM requirements are adequate** ☒Complete

Temporary Stockpiles (Soil, Materials, and Wastes)

3. Are stockpiles of soil, etc. anticipated during construction? ☐Yes ☒No

   (a) Select WM-3 (Stockpile Management), SS-3 (Hydraulic Mulch), SS-4 (Hydroseeding), SS-5 (Soil Binders), SS-7 (Geotextiles, Mats, Plastic Covers, and Erosion Control Blankets), or a combination as appropriate to cover temporary stockpiles of soil, etc. ☐Complete

EXAMPLE ONLY

(b) Select linear sediment barrier such as SC-1 (Silt Fence), SC-5 (Fiber Rolls), SC-6 (Gravel Bag Berm), SC-8 (Sand Bag Barrier), SC-9 (Straw Bale Barrier), or a combination to encircle temporary stockpiles of soil, etc. (Coordinate with District Construction for selection and preference of BMPs related to stockpiles.) ☐Complete

(c) Designate as a separate contract bid line item if the requirements in Construction Site Management (SSP 07-346) are anticipated to be inadequate or if requested by Construction. ☐Complete

4. Is there a potential for dust and debris from construction material (fill material, etc.) and waste (concrete, contaminated soil, etc.) stockpiles to be transported offsite by wind? ☐Yes ☒No

(a) Select SS-7, temporary cover, plastic sheeting or other BMP to cover stockpiles subject to wind erosion year-round, especially when significant wind and dry conditions are anticipated during project construction. (Coordinate with District Construction for selection and preference of wind erosion control BMPs.) ☐Complete

(b) Designate as a separate contract bid line item. ☐Complete

EXAMPLE ONLY

EXAMPLE ONLY
